




Fire Station #1 Project

Project Cost Update

June 17, 2020

CAPEX | PROJECT | ADVISORY

Tender Prices

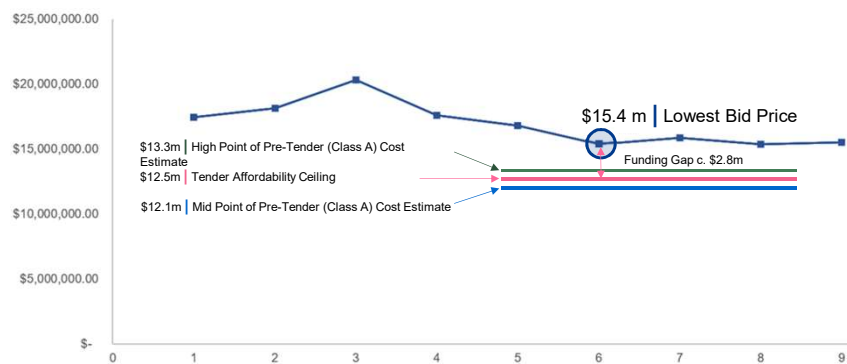

9 Bids
Submitted


4 Bids
Within 3.5%

CAPEX | PROJECT | ADVISORY

Construction Cost Estimation



- A baseline cost estimate was developed in 2017 by a professional quantity surveyor – this was the basis of the \$17M Budget
- The construction cost estimate was updated at each of 3 stages of project development.
- Each estimate indicated the project was likely affordable (in a pre-pandemic market).

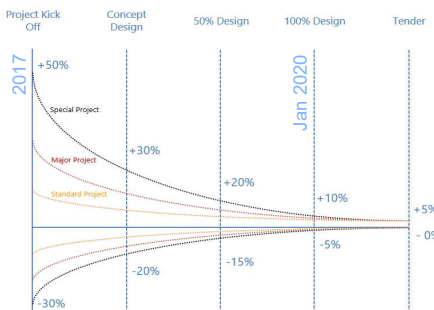

Extract from City of Nanaimo Project Management Framework, showing degree of confidence that should be communicated alongside the Project Budget at each stage of project development

NB: the City's Project Management Framework requires that, should the forecast cost of a project vary as the project progresses, there are two options: mitigate cost (which has already been done to deal with GFA and escalation cost pressures), or otherwise secure an increase in the Approved Project Budget.

CAPEX | PROJECT | ADVISORY

What's changed since 2017?



- 1 Escalation**
 ↑ 10% Additional
 Construction cost escalation to date has been around 10% > than forecast in 2017
- 2 GFA (M²)**
 ↑ 1/3 Increase
 The actual space program required to provide a functional facility was identified as being larger than assumed in 2017
- 3 COVID-19**
 Cost of Restrictions Continuing Included
 Budget did not include costs associated with the impacts of the Pandemic

CAPEX | PROJECT | ADVISORY

How have we mitigated cost pressure?



1 Cost / m² ↓ over 10%

- Total Project Cost / m² is down over 10%
- Construction Rate unchanged at \$7,100/m²
- Total Project Soft Costs down \$100k

2 Site Planning Avoided Significant Unnecessary Costs

Innovative Site Development Strategy implemented to avoid requirement for a temporary fire station during construction

3 Competition Secured a competitive market price

Market Engagement Strategy attracted a great deal of interest and price competition, demonstrated by number and distribution of tender prices

CAPEX | PROJECT | ADVISORY

Best Practice Delivery



- Steering Committee
- Stage Gate Process
- Cost Consultant (QS)
- Value Engineering
- Market Engagement
- Site Development Strategy
- Engagement of an Architect Specializing in Fire Station Design
- Validation of Functional Program



© 2015 Capex Project Advisory Services Inc.

CAPEX | PROJECT | ADVISORY

Schedule



COVID-19

Supply chain disruption

Labour availability

Labour productivity

Health & Safety overhead

- The Project is on schedule, despite the Pandemic
- The tender documents require the General Contractor to manage the risk of late delivery even if the restrictions continue to be in place for the duration of the project
- This has undoubtedly put upward pressure on the tender price but brings greater time and cost certainty

CAPEX | PROJECT | ADVISORY

Summary



- The Project is on-time but is over-budget despite the application of project control and governance best practices.
- A firm and competitive Tender is open for acceptance which provides a good degree of certainty that the new facility will be occupied by the summer of 2022 within a re-baselined budget of \$20m.
- To defer and re-tender the Project at a later date means that it will no longer be delivered in 2022, while at the same time deterring future tender participation and providing no guarantee or likelihood of reducing cost.

CAPEX | PROJECT | ADVISORY
